




## EVALUATION SNAPSHOT

## URBAN TRANSFORMATION

# CITY WISE DISTRIBUTION OF SAMPLE SIZE

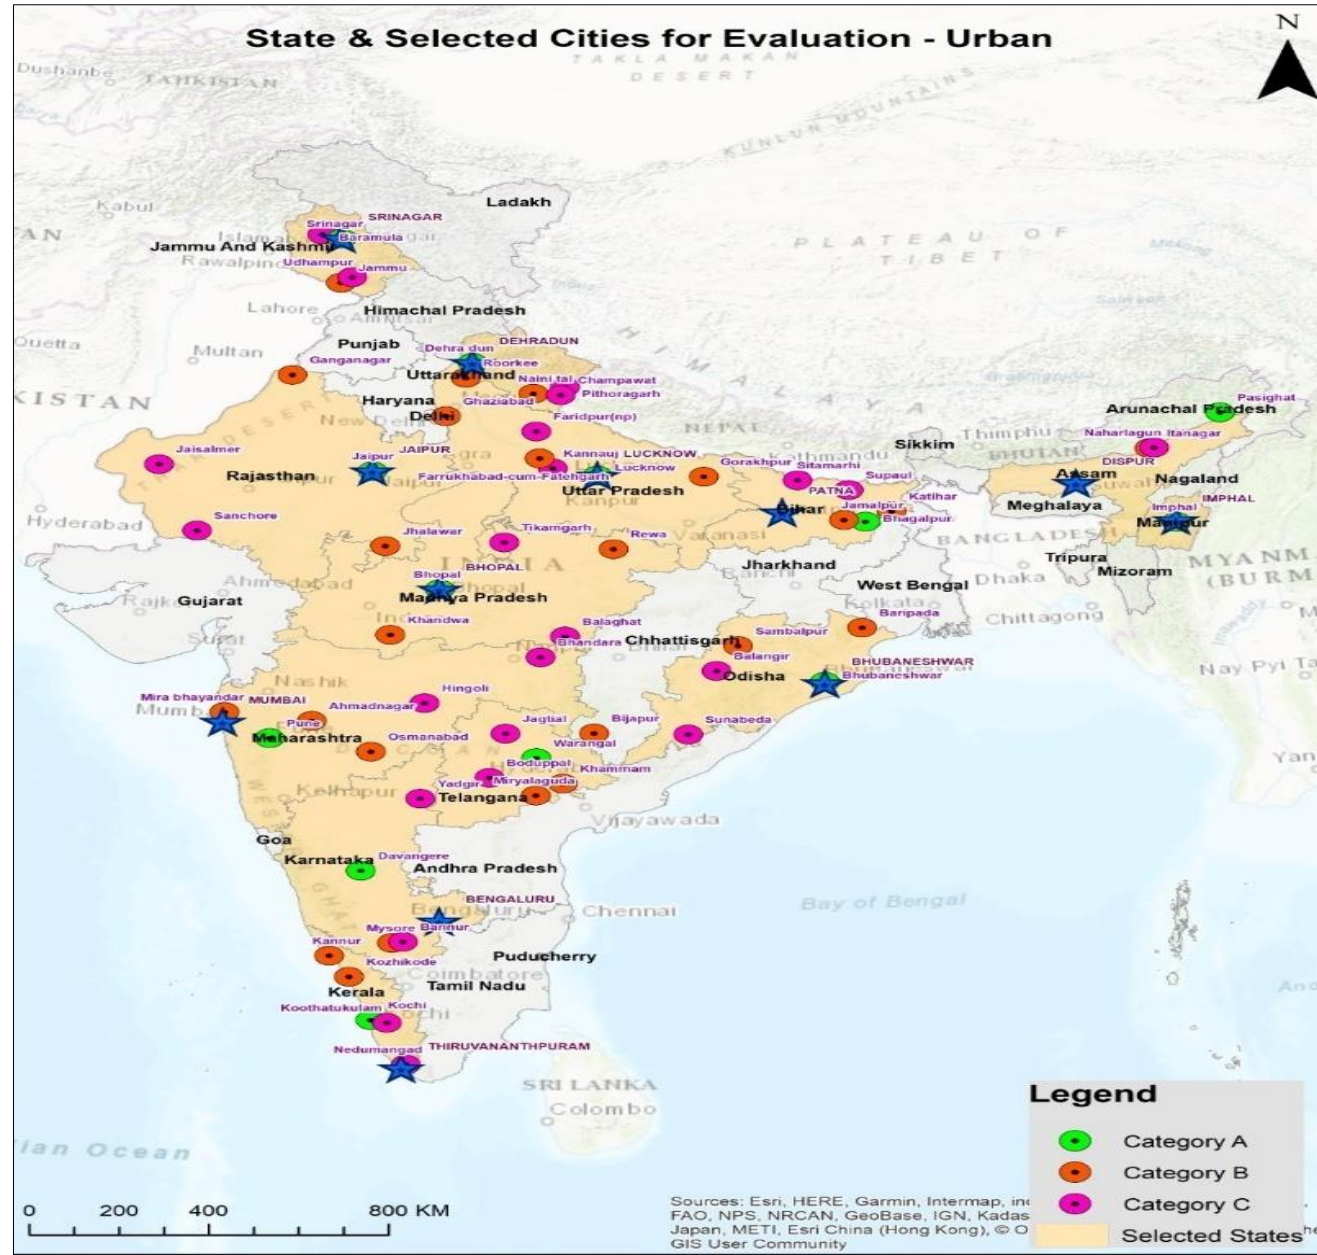

# PRADHAN MANTRI AWAS YOJANA – URBAN (PMAY-U)

Table 3-5: Distribution of Housing Shortage among different Economic categories as on 2012

| Category      | Distribution of Housing Shortage among different Economic categories as on 2012 |               |
|---------------|---------------------------------------------------------------------------------|---------------|
|               | No. (In millions)                                                               | In Percentage |
| EWS           | 10.55                                                                           | 56.18         |
| LIG           | 7.41                                                                            | 39.44         |
| MIG and above | 0.82                                                                            | 4.38          |
| Total         | 18.78                                                                           | 100.00        |

Source: Report of the technical group (TG-12) on urban housing shortage 2012-2017 by Ministry of Housing and Urban Poverty Alleviation (MoHUPA), GOI.

According to the Ministry of Housing and Urban Affairs (MoHUA), the urban housing shortage was estimated at 18.78 million units in 201213, primarily affecting the EWS and Low-Income Groups (LIG).

| Component  | Sanctioned (Lakh) | Houses Grounded (Lakh) | House Completed (Lakh) | Occupied (Lakh) |
|------------|-------------------|------------------------|------------------------|-----------------|
| BLC        | 73.58             | 68.01                  | 51.88                  | 51.88           |
| CLSS / ISS | 25.04             | 25.04                  | 25.04                  | 25.04           |
| AHP        | 14.15             | 14.28                  | 9.28                   | 5.54            |
| ISSR       | 1.74              | 1.71                   | 1.46                   | 1.18            |
| Total      | 114.51            | 109.04                 | 87.66                  | 83.63           |

Source: <https://pmay-urban.gov.in>

As on June 2025, Out of the 114.51 lakh sanctioned, 87.95 lakhs is occupied (77%). This shows almost 50% of the housing shortage estimated by the technical group (TG-12) is full-filled during 2015-2025.

Figure 4-17: Beneficiary Response to challenges faced

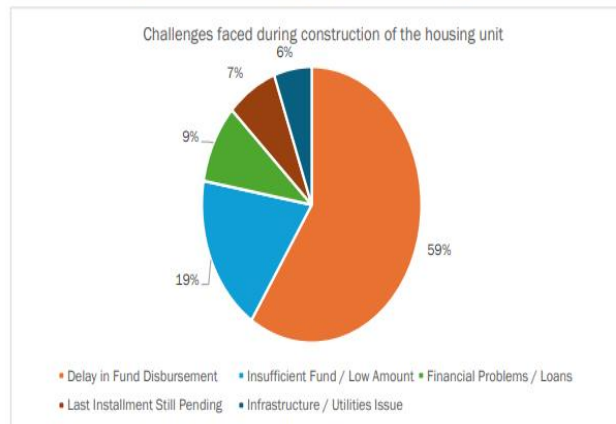


Figure 4-19: BLC performance across different city sizes


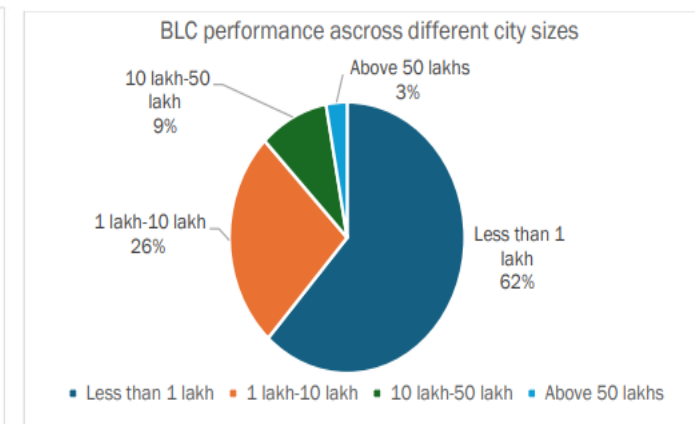


Figure 4-39: Year-wise Physical Progress of Houses under AHP



Source: <https://pmay-urban.gov.in>

Beneficiary-Led Construction has been more effective in reaching smaller cities and towns, while AHP is better suited for larger and metropolitan cities. However, AHP has witnessed slow uptake, with occupancy lagging behind.

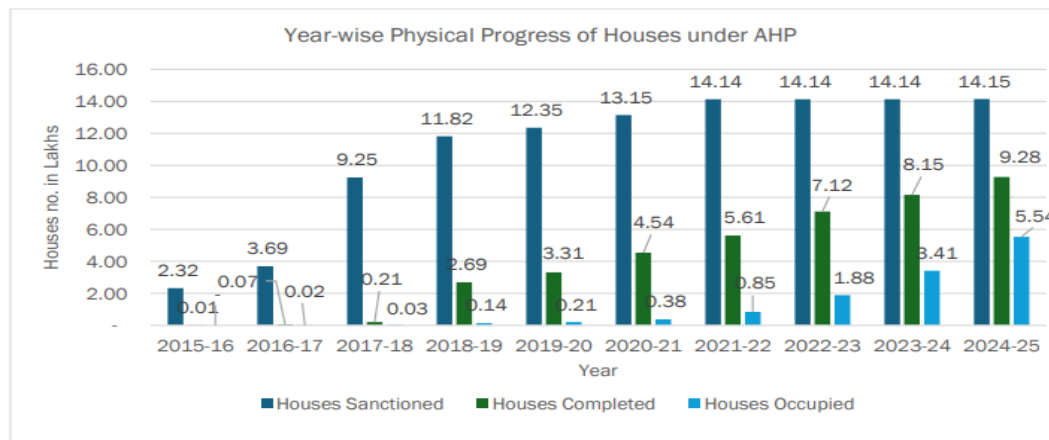

# PRADHAN MANTRI AWAS YOJANA – URBAN (PMAY-U)

The Affordable Rental Housing Component (ARHC) component, introduced as a sub-scheme, aims to provide affordable and hygienic living spaces, particularly for urban migrants and industrial workers.

Table 7: Summary Progress of ARHC Houses

| S. No. | Items                               | Model - 1: Government funded Vacant Houses available for ARHCs | Model - 2: ARHC units through Public/Private Entities | Total                  | Percentage (%)   |
|--------|-------------------------------------|----------------------------------------------------------------|-------------------------------------------------------|------------------------|------------------|
| A.     | Target - ARHC Houses                | -                                                              | -                                                     | 2,95,000 <sup>37</sup> |                  |
| B.     | Total ARHC Houses under development | 83,534 <sup>38</sup>                                           | 82,273 <sup>39</sup>                                  | 1,65,807               |                  |
| C.     | Completed                           | 5,783                                                          | 36,450                                                | 42,233                 | 14% of Target    |
| D.     | Handed Over (Occupied)              | 4,605                                                          | -                                                     | 4,605                  | 11% of Completed |
| E.     | Others                              |                                                                |                                                       |                        |                  |
| E.1    | Construction work under progress    | No information                                                 | 19,621                                                | 19,621                 | 7% of Target     |

A total of 42,233 houses are completed, which represents 14% of the overall target of 2,95,000 ARHC houses. Of the completed units, only 4,605 houses have been handed over for rental, which is just 11% of the completed stock

While there is strong coherence among all the urban schemes, there is a lack of Integrated Databases Across MoHUA Centrally Sponsored Schemes (CSSs). This lack of integration means that beneficiaries have to undergo repetitive enrolment processes and resubmit documents for each scheme (for e.g., a PMAY-U housing beneficiary also seeking an Ujjwala LPG connection or SBM toilet)


AHP operational challenges has to be addressed. The scheme must expedite regulatory approvals such as building plan approvals, environmental clearances, and RERA registration.

To address the exclusion of many urban poor, particularly tenants and migrant workers, due to documentation, ARH may specifically refine its targeting and eligibility criteria. This could involve simplifying documentation, accepting alternative forms of identification.

# Swachh Bharat Mission(SBM)


1. These responses suggest timely service delivery and financial processing for the majority of beneficiaries.

Figure 5-10: Beneficiary responses on IHHL implementation

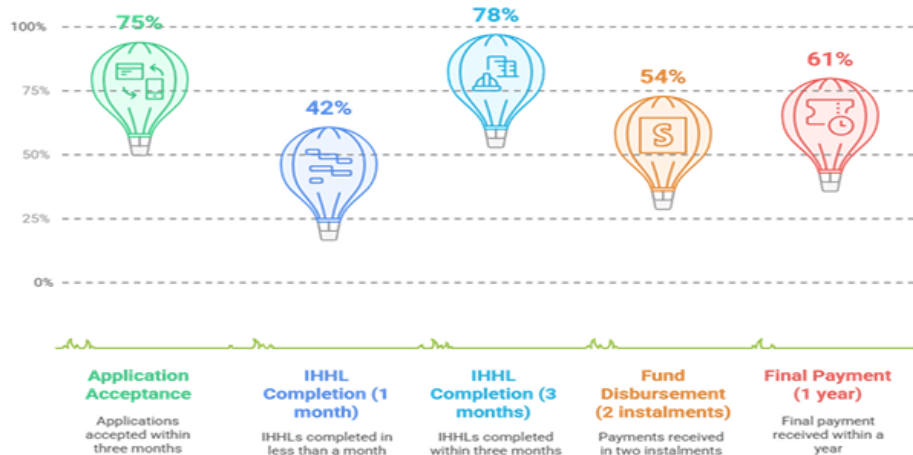

2. Data show good connectivity of waste disposal systems through septic tanks.


Figure 5-16: Status of Toilet discharge

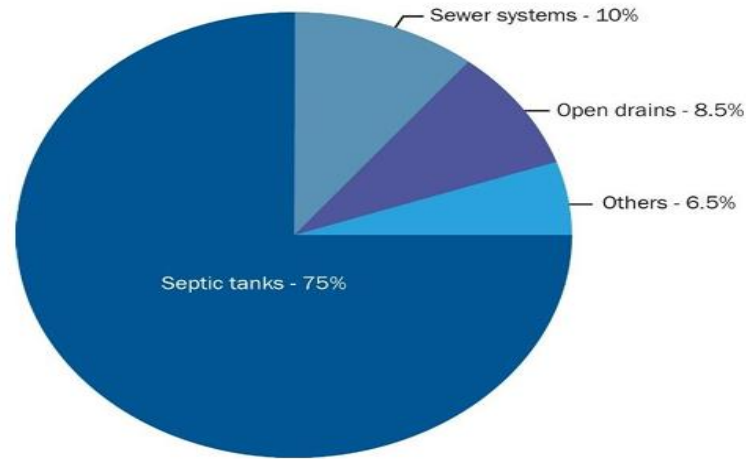

Source: Primary HH survey

3. Households accessed septic tank de-sludging services via ULBs.

Figure 5-17: Desludging of septic tank using ULB/ Private services

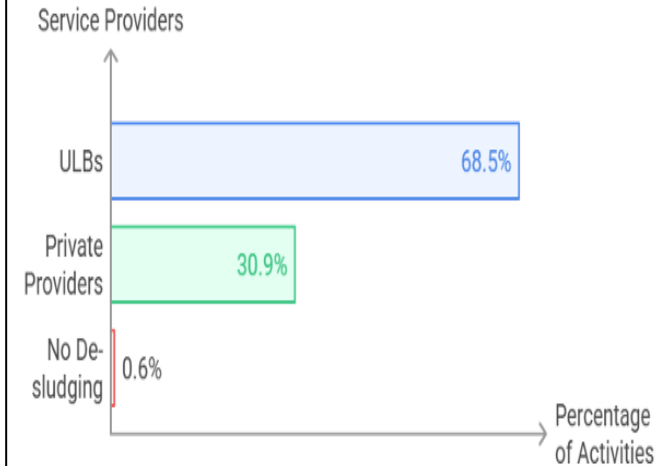

## 4. Legacy Waste Management

A total of 2,417 dumpsites (with more than 1,000 tonnes of waste) have been identified for remediation, which collectively occupy 14,732.66 acres of land. Of which, 11.38 crore MT (48%) is remediated, and 5,900 Acres (40%) area reclaimed. **More than half of the waste (52%) and 60% of the land area remain unremediated.**

Figure 5-8: Challenges faced by ULBs



Source: Primary data analysis

**Wide inter-state disparities persist in SBM implementation, with liquid waste management requiring additional attention across states.**

# Atal Mission for Rejuvenation and Urban Transformation


## 1. Physical Progress of the AMRUT 2.0

Table 6-3: Number of projects and amount approved in AMRUT

| Component                            | Sanctioned      |                    | Awarded         |                  |
|--------------------------------------|-----------------|--------------------|-----------------|------------------|
|                                      | No. of Projects | Amount in crores   | No. of Projects | Amount in crores |
| Water Supply                         | 3587            | 1,13,570.13        | 2148            | 60,563.10        |
| Sewerage & Septage Management        | 594             | 67,999.81          | 336             | 26,575.99        |
| Water Body Rejuvenation/ Storm Water | 3075            | 6,144.77           | 1737            | 3,304.36         |
| Parks & Green Space Development      | 1667            | 1,014.87           | 1016            | 553.20           |
| <b>Total</b>                         | <b>8923</b>     | <b>1,88,729.58</b> | <b>5,237.00</b> | <b>90,996.65</b> |


## 2. Data reveals the scope for further infrastructure strengthening for 24&7 water supply

Figure 6-7: Status of water supply after new connections

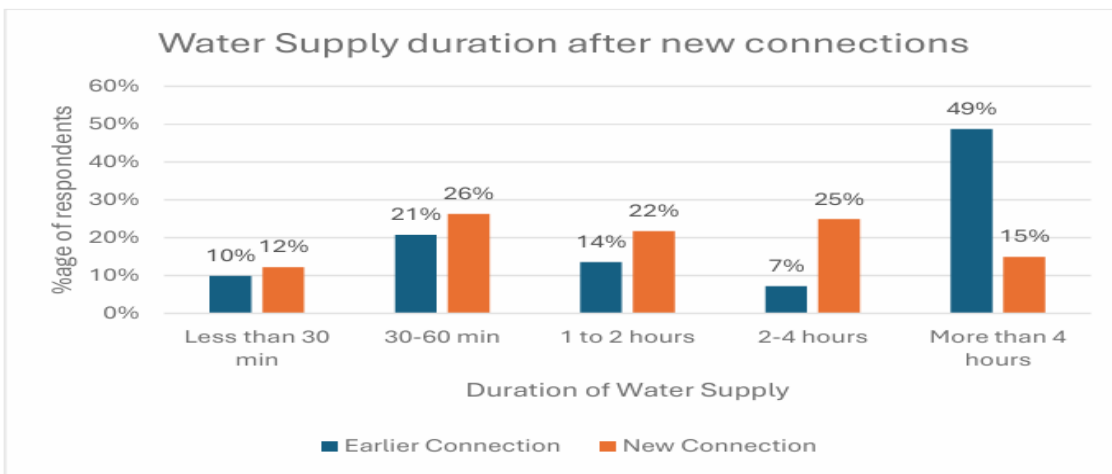


## 3. A majority of households are still not connected to formal sewer networks.

Figure 6-23: HH-Level Sewerage & Septage Disposal Mechanism

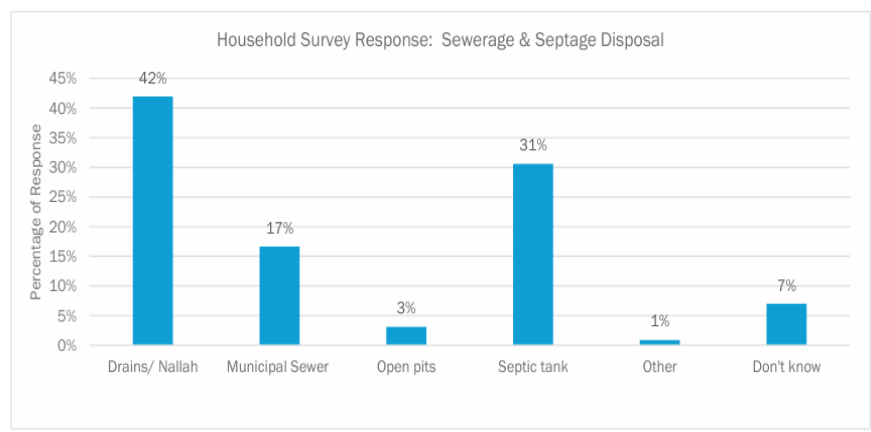

## 4. It reflects insufficient or inadequately maintained stormwater infrastructure.

Figure 6-25: Household Response to Discharge of Stormwater

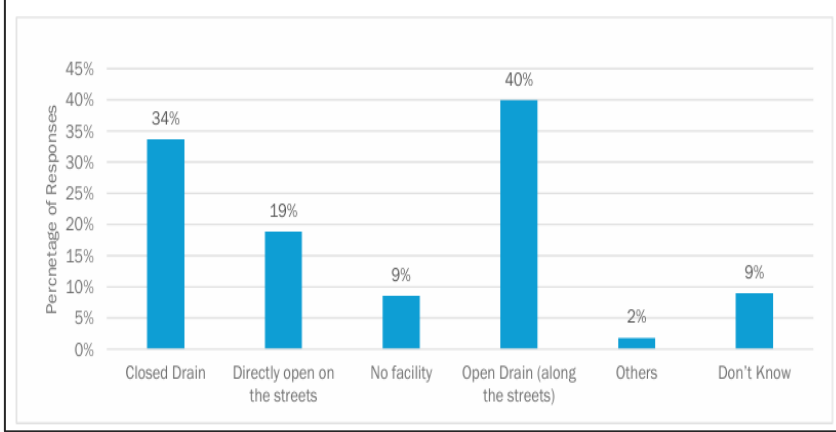

Despite infrastructure growth, coverage remains limited in marginalised settlements and peri-urban areas, indicating equity and inclusion gaps. Encourage ULBs for post-project O&M frameworks through bylaws and MoUs with SHGs. Build capacity to promote localised asset management.

# Deendayal Antyodaya Yojana – National Urban Livelihoods Mission (DAY-NULM)

Figure 7-12: Change in Income level (Last year vs Current Year) among SHGs in SM&ID




Figure 7-7: EST&P- Year-on-Year Progress on Candidates Targeted, Trained and Placed

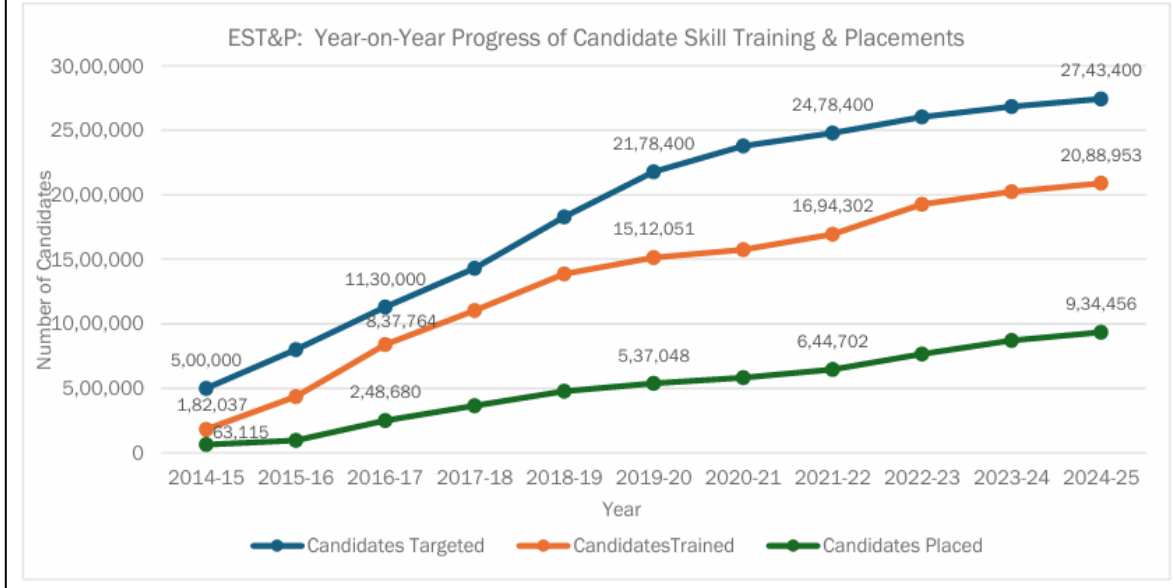


Figure 7-16: SEP - State-wise progress of Enterprises formed


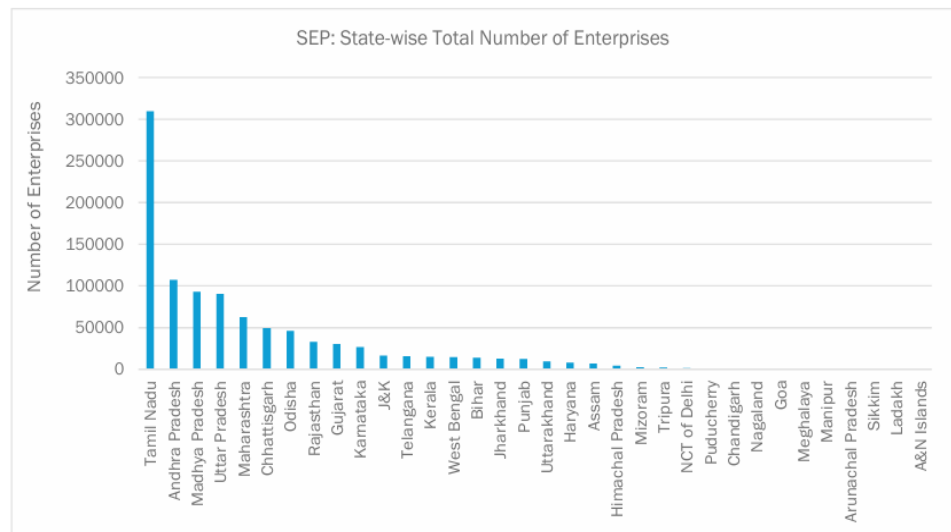


Figure 7-29: Beneficiaries from Vulnerable Categories - SUSV



# Smart Cities Mission (SCM)

**1. The Smart Cities Mission covers 100 cities across India, selected through a multi stage competitive process.**


**Table 8-1: Round-wise selection of Smart Cities**

| Rounds                 | Round 1      | Fast Track | Round 2        | Round 3   | Round 4                            |
|------------------------|--------------|------------|----------------|-----------|------------------------------------|
| No. of cities selected | 20           | 13         | 27             | 30        | 10                                 |
| Date of selection      | January 2016 | May 2016   | September 2016 | June 2017 | 9 in January 2018 & 1 in June 2018 |


Source: Smart Cities Mission: An Evaluation by Standing Committee on Housing and Urban Affairs (2023-24)

**2. Out of 100 cities, 29 cities have achieved 100% project implementation while 71 cities are yet to complete all the project implementation.**

**Figure 8-2: Nos. of Projects and Total Project cost (in INR crore)**

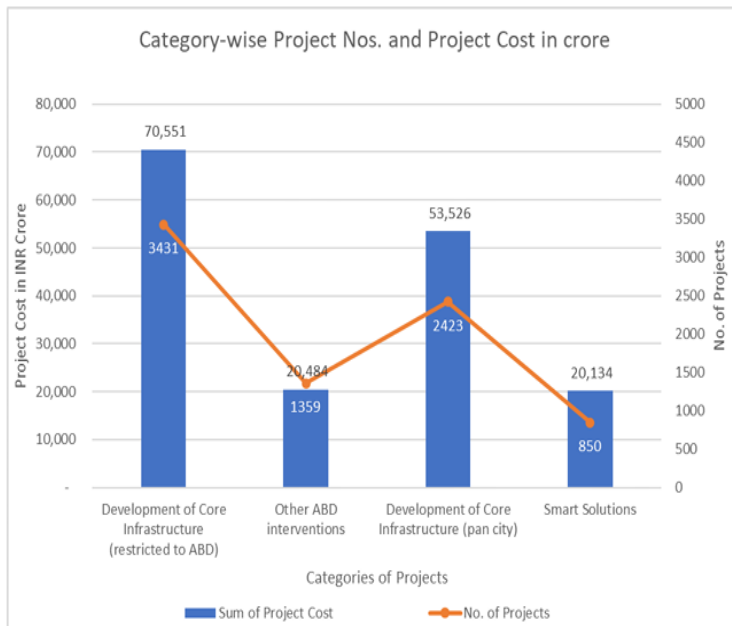


**Figure 8-5: List of cities with less than 80% completion**

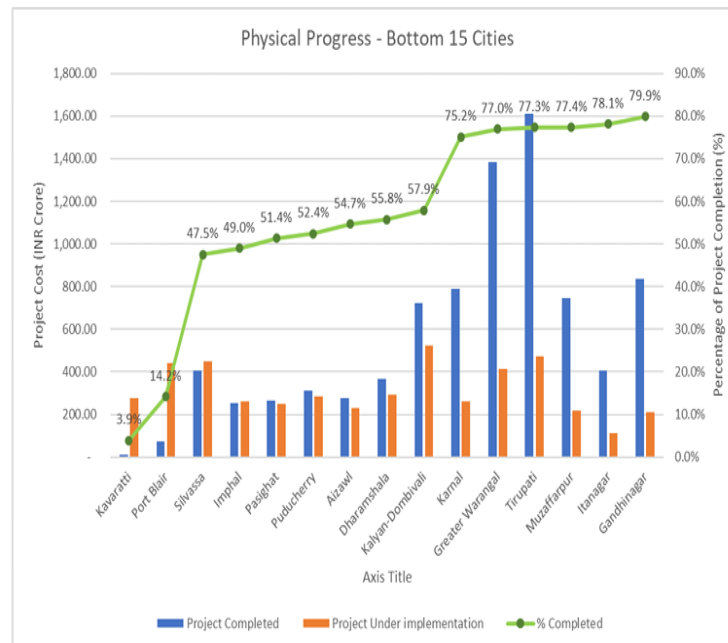

**3. Improvements across service under SCM**

**Figure 8-23: Perception on Improvements across services due to SCM**

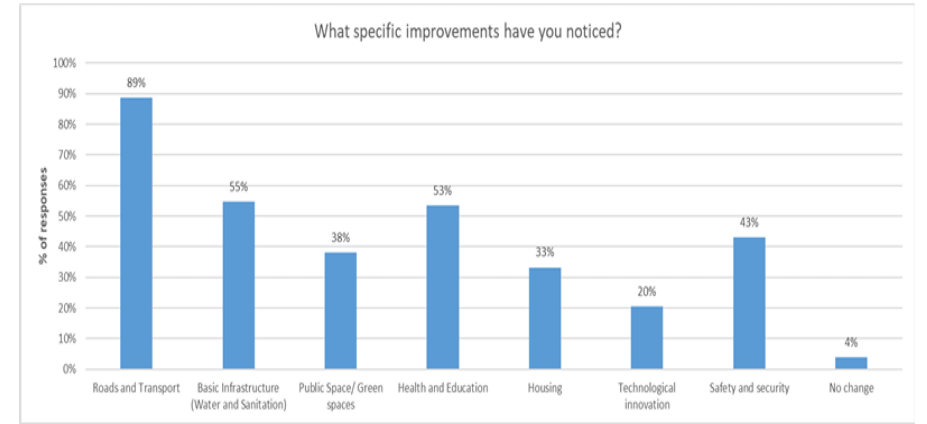

**Figure 8-24: Public feeling safer due to installation of surveillance cameras**

